


HawaiiBusiness' 2018 *Best Places to Work*



Week of 3/3/19

*Construction
Management By:*

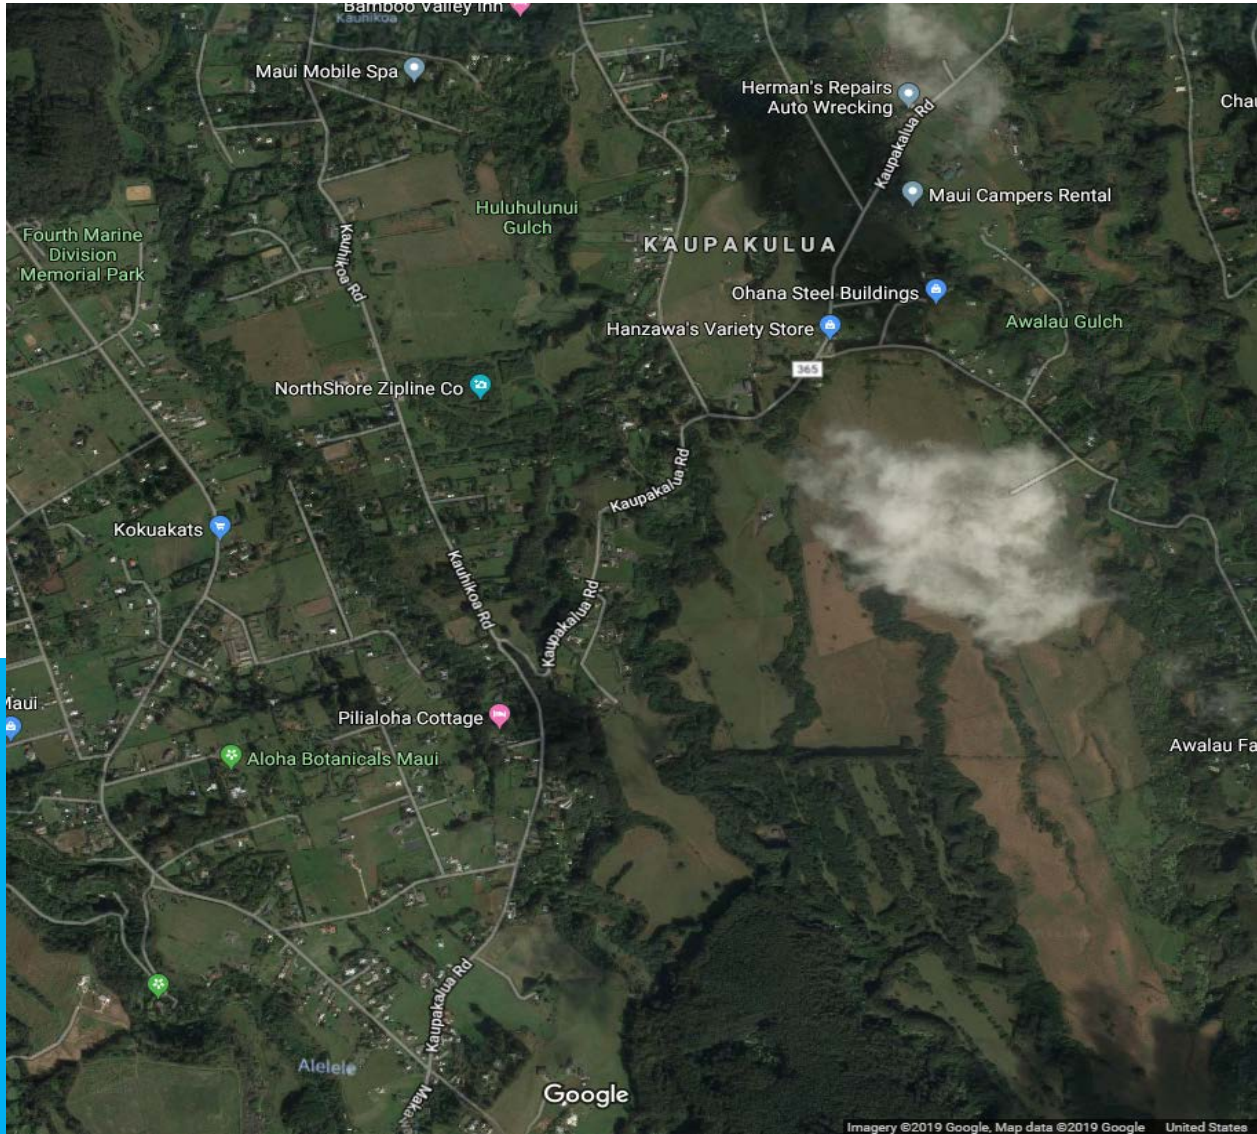

Kaupakalua Rd Pavement Reconstruction

Kokomo Rd to E. Kuiaha Rd

Island of Maui

Project Number: STP-0365(010)

Project Scope:

This project involves the removal of existing pavement down to the gravel subbase within the road right-of-way, installation of a new asphalt concrete pavement section with reinforcing geogrid, new rigid pavement (Portland Cement Concrete) section for a small portion of the roadway, installation of new pavement striping and pavement markers, adjusting manhole and valve frames and covers where needed, removal/replacement of dented guardrails, removing/replacing signage & posts, and other incidental items.

When:

Notice to Proceed: February 11, 2019

Contract Working Days: 287

Anticipated Completion Date: April 7, 2020 // Revised Completion Date: April 13, 2020

Roads Involved:

Kaupakalua Rd from Kokomo Rd to E. Kuiaha Rd

Contractor:

HI-Built, LLC
72 Tings Dr
Wailuku, HI 96793

Contract Amount:

\$4,796,353.55

Project Contact:

County of Maui, Department of Public Works
Engineering Division
(808) 270-7745

Construction Update:

Work Scheduled Week of 2/24/19 – 3/2/19:

- Continue potholing waterlines

Work Scheduled Week of 3/3/19 – 3/9/19:

- No work scheduled to take place



Kaupakalua Rd
