


HawaiiBusiness' *2018 Best Places to Work*



Week of 7/27/19

**Construction
Management By:**

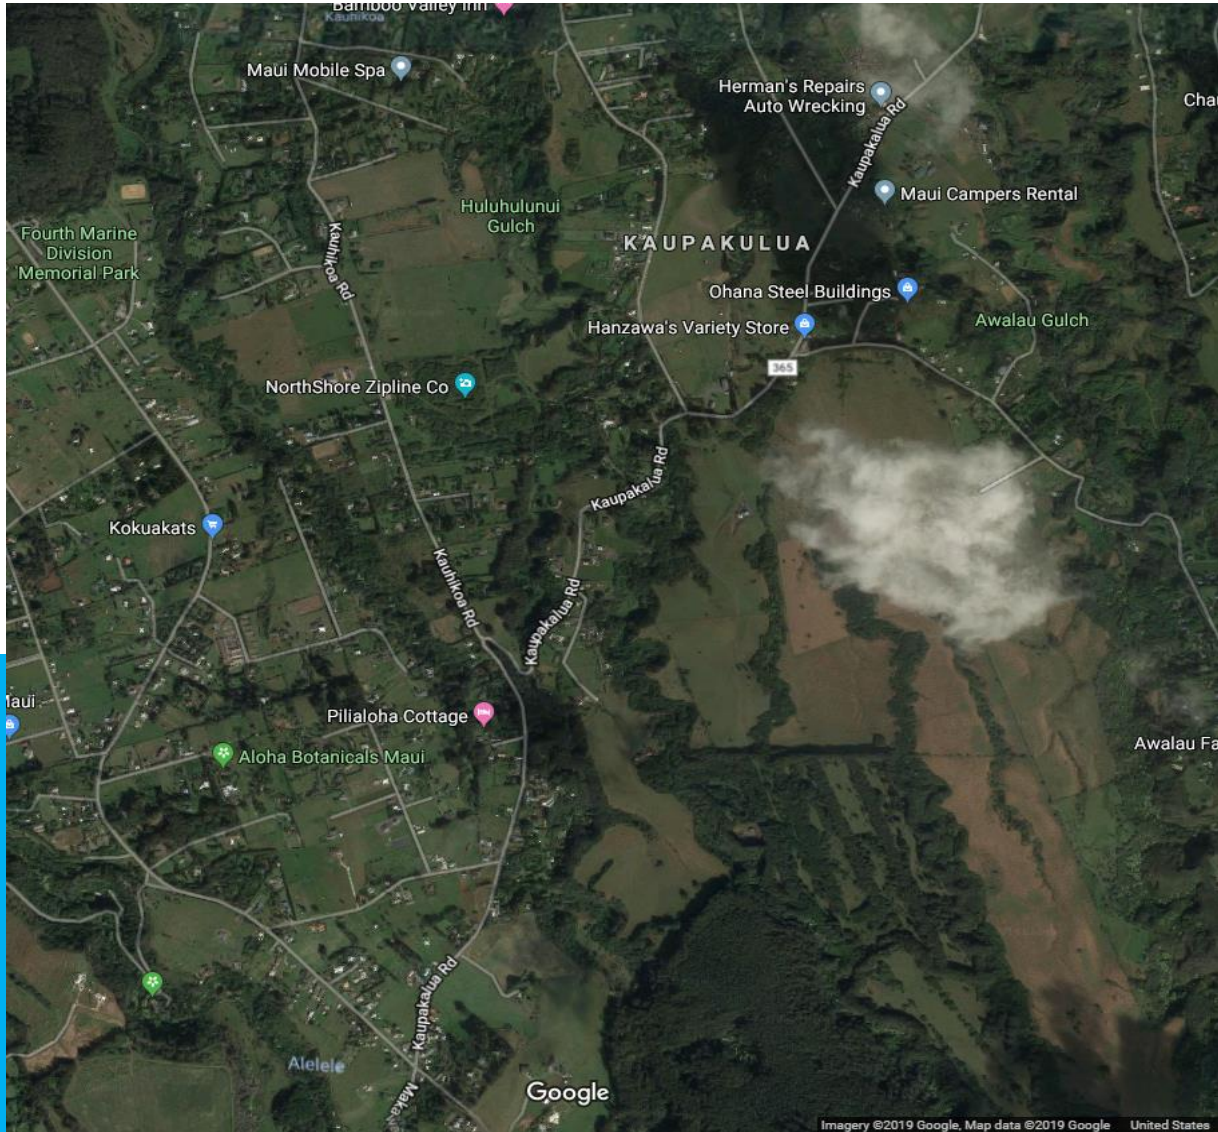

Kaupakalua Rd Pavement Reconstruction

Kokomo Rd to E. Kuiaha Rd

Island of Maui

Project Number: STP-0365(010)

Project Scope:

This project involves the removal of existing pavement down to the gravel subbase within the road right-of-way, installation of a new asphalt concrete pavement section with reinforcing geogrid, new rigid pavement (Portland Cement Concrete) section for a small portion of the roadway, installation of new pavement striping and pavement markers, adjusting manhole and valve frames and covers where needed, removal/replacement of dented guardrails, removing/replacing signage & posts, and other incidental items.

When:

Notice to Proceed: February 11, 2019

Contract Working Days: 287

Anticipated Completion Date: April 7, 2020 // Revised Completion Date: April 13, 2020

Roads Involved:

Kaupakalua Rd from Kokomo Rd to E. Kuiaha Rd

Contractor:

HI-Built, LLC
72 Tings Dr
Wailuku, HI 96793

Contract Amount:

\$4,796,353.55

Project Contact:

County of Maui, Department of Public Works
Engineering Division
(808) 270-7745

Construction Update:

Work Completed Week of 7/21/19 – 7/27/19:

- No work scheduled to take place

Work Scheduled Week of 7/28/19 – 8/3/19:

- No work scheduled to take place
