



Week of 12/21/19

*Construction
Management By:*



Molokai Baseyard Facility

7 Pueo Place (Molokai Industrial Park)

Island of Molokai
Project Number: 14-32

Project Scope:

The new baseyard will consist of one Administrative Building, approximately 2,560 SF, one Maintenance Building, approximately 7,440 SF, and one Vehicle Storage Building, approximately 3,960 SF, located in Naiwa, Molokai

When:

Notice to Proceed: January 8, 2018

Contract Calendar Days: 550 / Amended Contract Days: 697

Original Completion Date: July 12, 2019 / Revised Completion Date: Jan 10, 2020

Roads Involved:

Pueo Place, off of Ulili Street

Contractor:

F&H Construction
1728 Wili Pa Loop, Suite 200
Wailuku, HI 96793

Contract Amount:

\$7,528,000.00

Project Contact:

County of Maui, Department of Public Works
Engineering Division
(808) 270-7745


Construction Update:

Work Completed Week of 12/15/19 –12/21/19:

- Site Grading
- Site Concrete
- Irrigation
- Site Paving

Work Scheduled Week of 12/22/19 –12/28/19:

- Cont. Site Paving
- Irrigation/Landscape
- Cont. Site Grading
- Install Vehicle Lift
- Finish Work

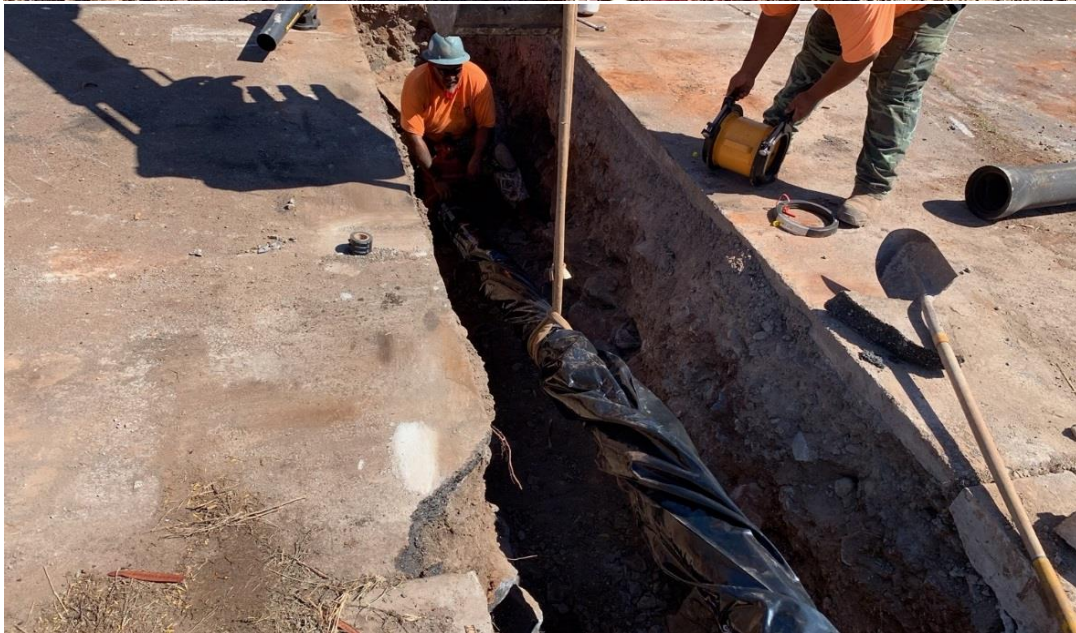

Molokai Baseyard Facility
